


POMONA PROGRAM MANAGEMENT

STUDY - WATER SERVICE LATERAL REPLACEMENT, PROJECT NO: 595-95006


PROJECT CATEGORY: VARIOUS WATER PROJECTS

Contractor	
Contract Award	
Limited NTP	
NTP	
Completion	
Revised Completion	
Original Contract Value	\$ 25,000.00
Change Orders this Month	
Amended Contract Value	
Earned to Date	

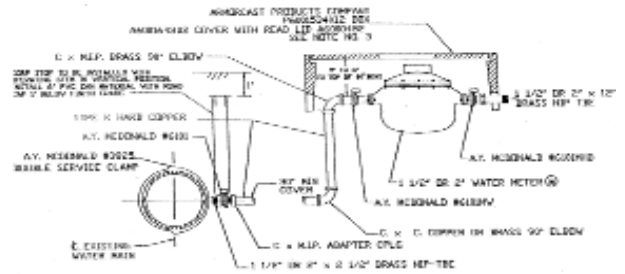

PROGRESS SUMMARY

Project Definition & Viability	100%
Design RFP	0%
Selection Process	0%
Pre-Design Consultant Meeting	0%
Constraints Recommendations & Support Services	0%
Design Plan & Submittal	0%
Final Bid Document	0%
Construction Advertising	0%
Bid Opening & Award of Construction	0%
Construction & Construction Management	0%
Project Close Out/Completion	0%

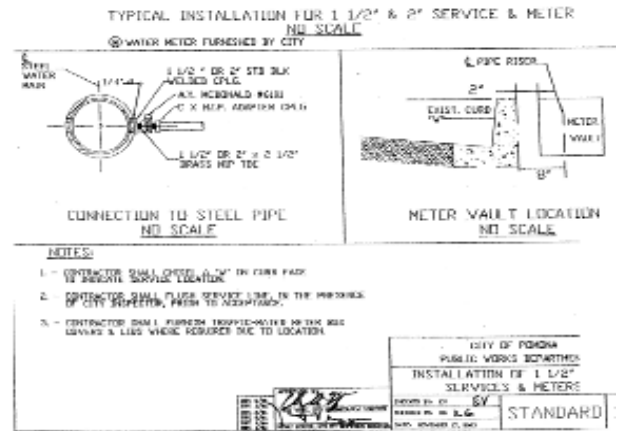

SAFETY & SECURITY ISSUES

Time Lost Injury Status	None
Incidents this Month	None
Security	None
Initial Event Reports	None

WORK ACCOMPLISHED IN JULY

Submitted draft specifications through City for review.
 Received City's comments pursuant to review of draft specifications.

UPCOMING WORK NEXT MONTH

Incorporate City comments in draft specifications and resubmit for final review.

